ELKEM ASA TECHNOLOGY

Master Schedule & Portfolio Control Report

Fiskå Industrial Park, Kristiansand | EIA-748 EVM & IFRS 15 Governance Hub

Executive Briefing: This report integrates the master project schedule, EIA-748 Earned Value Management (EVM) metrics, IFRS 15 over-time revenue recognition, and SkatteFUNN / Enova public grant compliance across Elkem ASA Technology's active R&D; and pilot plant portfolio at Fiskå Industripark.

1. Active Portfolio Performance Summary (EIA-748 EVMS)

Control Account (CA) / Project Name	Grant Body	BAC (NOK)	PV / BCWS	EV / BCWP	AC / ACWP	CPI	SPI	EAC (NOK)
CA-2045: Fiskå Carbon-Neutral Pilot	Enova	45,000,000	22,500,000	21,000,000	23,400,000	**0.897**	**0.933**	50,142,857
CA-1042: Furnace Automation Twin	NFR	10,000,000	4,000,000	3,500,000	3,800,000	**0.921**	**0.875**	10,857,143
CA-3080: NextGen Battery Anode R&D;	SkatteFUNN	15,000,000	8,000,000	8,200,000	7,900,000	**1.038**	**1.025**	14,451,220

2. Dynamic Gantt of Gantts — Master Portfolio Schedule

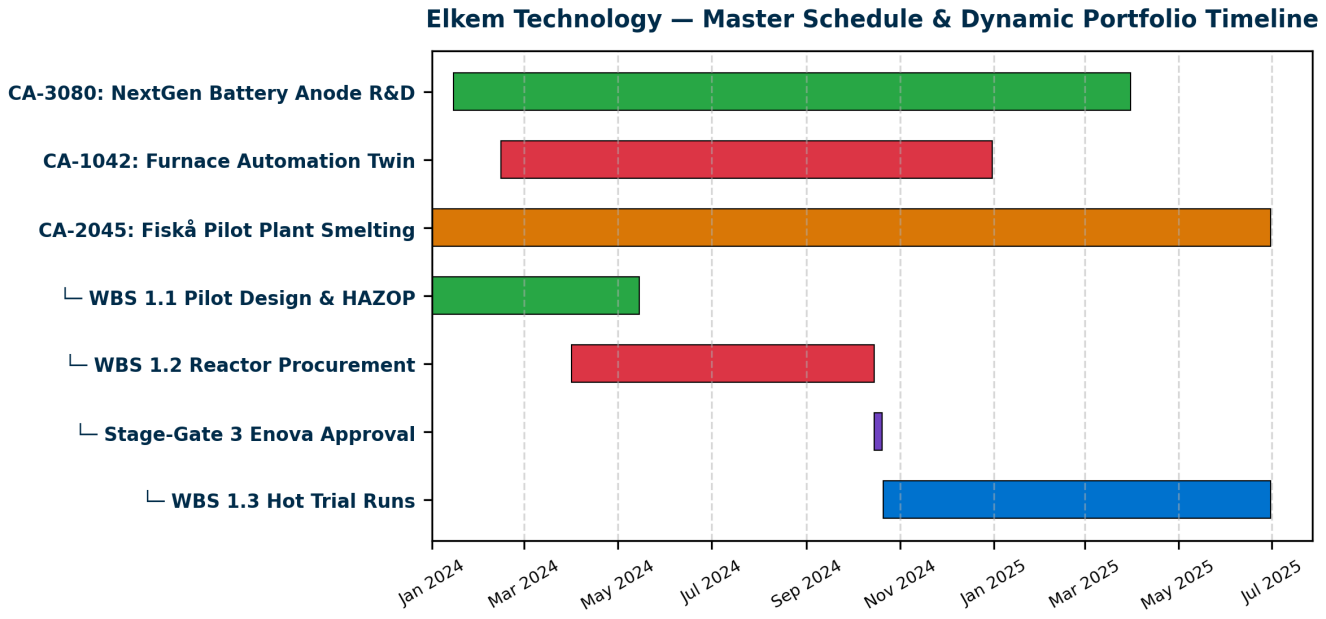


Figure 1: Hierarchical Gantt of Gantts showing Master Projects, WBS Level 2 packages, and Stage-Gate 3 Enova Milestone.

3. IFRS 15 Revenue Control & Public Grant Compliance

Project ID / Grant Scheme	Contract Value	PoC % (ACWP/EAC)	Recognized Rev.	Invoiced YTD	Contract Asset	Statutory Audit Status
CA-2045 (Enova Grant)	55,000,000 NOK	46.67 %	25,668,500 NOK	20,335,167 NOK	**+5,333,333 NOK**	**Compliant**
CA-1042 (NFR Grant)	12,500,000 NOK	35.00 %	4,375,000 NOK	3,000,000 NOK	**+1,375,000 NOK**	**Compliant**
CA-3080 (SkatteFUNN #298412)	18,000,000 NOK	54.67 %	9,840,600 NOK	9,320,600 NOK	**+520,000 NOK**	**RF-1053B Approved**

> **Governance & COSO 2013 Control Line:** All forecast changes (EAC) and baseline adjustments require Human-in-the-Loop (HITL) approval from the Lead Technology Controller. Every decision is cryptographically signed and logged into an immutable SHA-256 audit chain meeting EU AI Act Article 12 & 14 requirements.
